DRAFT FOR DISCUSSION PURPOSES 1/12/02

ID	Task Name	Duration	Start	Finish	Predecessors
1	**Short Term Study: EHC**	**221 days**	**Thu 11/1/01**	**Fri 8/30/02**	
2	Investigator Brochure	15 days	Thu 11/1/01	Wed 11/21/01	
3	Study Objectives Complete	~~5~~ 0 days	Thu 11/1/01	Wed 11/7/01	
4	Draft protocol ~~/ Summary Plan~~ (Lincoln)	10 days	Thu 11/8/01 [Date] Wk	Wed 11/21/01	3 week of Thg.
5	Site Selection Complete	~~15~~ 0 days	Thu 11/22/01 [Date] Wk	Wed 12/12/01	4
6	1st Project Agreement with CRO [Prot. develop]	15 days	Thu 12/13/01	Wed 1/2/02 1/25/02	5,4
7	Protocol Development 52 days	30 days	Thu 11/22/01	2/1/02	2,4 (5)
8	Final Protocol, Informed Consent	0 days	Wed 1/2/02 2/1/02	Wed 1/2/02 2/1/02	7
9	IRB Review	20 days	Thu 1/3/02 [February avail] BN	Wed 1/30/02	8,2
10	Bioanalytical Methods Setup at MDS (1st Spec.)	80 days	Thu 11/22/01	Wed 3/13/02	4
11	IRB Approval	0 days	~~Wed 1/30/02~~ [Date - BN]	~~Wed 1/30/02~~	~~9~~
12	2nd Project Agreement	10 days	Thu 1/31/02	Wed 2/13/02	11 [Completion of 6]
13	Recruitment and Screening	~~30~~ 20 days	Thu 2/14/02	Wed 3/13/02	~~9~~ 11 [11] 11,12
14	Test Materials Available 4 weeks external Pathologist	~~0~~ days	Thu 3/14/02	Thu 3/14/02	
15	**Clinical Performance**	**11 days**	**Thu 3/14/02**	**Sun 3/24/02**	**14,13,11**
20	**Lab Analysis**	**40 days**	**Mon 3/25/02**	**Fri 5/17/02**	**10,15**
24	**Data Management**	**65 days**	**Mon 3/25/02**	**Fri 6/21/02**	**15,20SS**
31	Draft Report	6 wks	Mon 6/24/02	Fri 8/2/02	24
32	Results Available	0 days	Fri 8/2/02	Fri 8/2/02	31
33	Final Report	20 days	Mon 8/5/02	Fri 8/30/02	32
34	Final Results	0 days	Fri 8/30/02	Fri 8/30/02	33

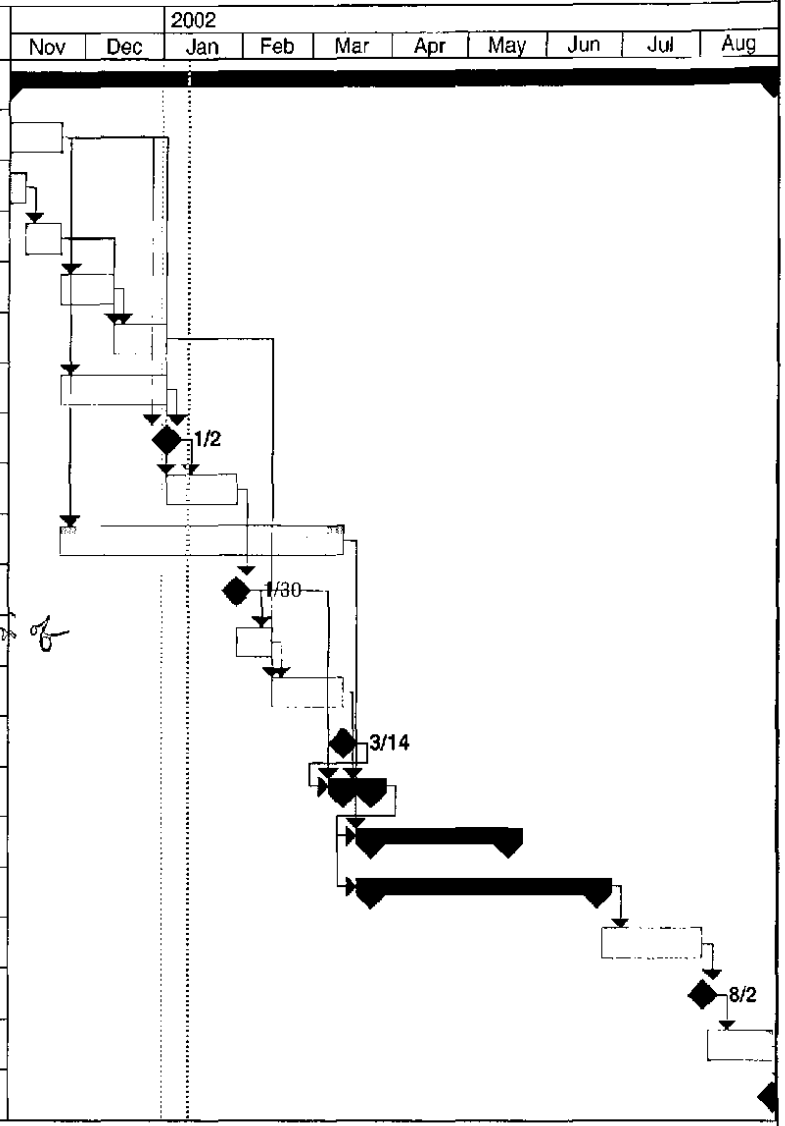

Project: Short Term2
Date: Fri 1/11/02

Task
Split
Progress
Milestone
Summary
Rolled Up Task
Rolled Up Split
Rolled Up Milestone
Rolled Up Progress
External Tasks
Project Summary

PM3006787461

Source: https://www.industrydocuments.ucsf.edu/docs/nnmx0001
